

FOR UPDATES & UPCOMING MEETINGS ON THIS TOPIC:

Sign In Here



Scan the QR Code with the camera on your smartphone, then follow the link to the sign-in sheet.



GRANT UTK-8 SITE MODERNIZATION UPDATE

Wednesday August 28, 2024





WELCOME / INTRODUCTION

- MICHELE CAIN PRINCIPAL
- SAMER NAJI COMMUNICATIONS SUPERVISOR, FPC
- LEE DULGEROFF SDUSD SR. EXECUTIVE DIRECTOR, FPC
- FRANCISCO CAMPUZANO SDUSD PM SUPERVISOR
- ATHENA FONSECA SDUSD PROJECT MANAGER
- RALPH ROESLING RNT ARCHITECTS, PRINCIPAL-IN-CHARGE
- GEMMA HSIUEH RNT ARCHITECTS, PROJECT MANAGER







AGENDA


- PROJECTS COMPLETED
- CAMPUS MODERNIZATION UPDATE
- CAMPUS MODERNIZATION TIMELINE
- QUESTIONS/COMMENTS
- ADJOURN







PHASING FROM 2013 MASTERPLAN

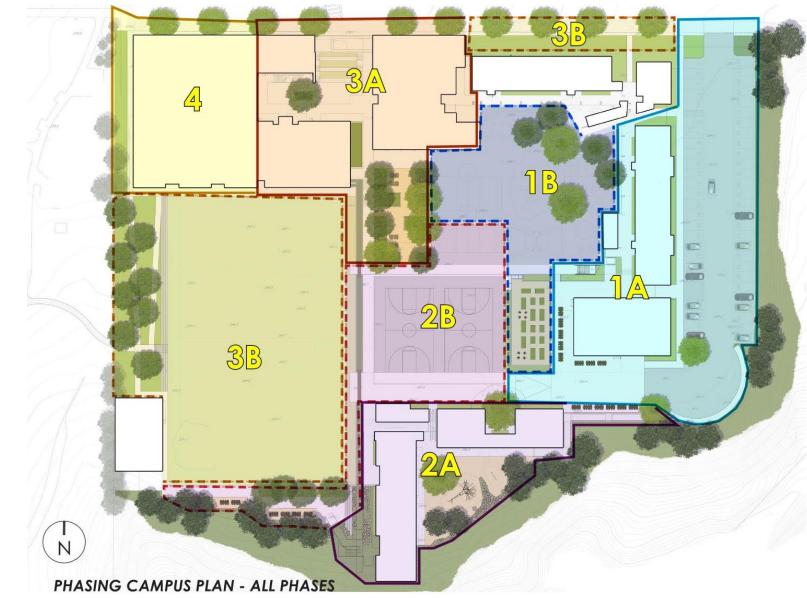





(from 04/09 Presentation)

PROJECTS COMPLETED

- 2-STORY CLASSROOM BUILDING, NORTH BUILDING #700 (Completed 2005)
- EROSION CONTROL AND PAVING (Completed 2016)
- WHOLE SITE MODERNIZATION PHASE 1

2-Story Classroom East Building #600, Food Service and Student Lunch Area, Teacher Workroom and Lounge, Expanded Parking (Completed 2017)

• FIELD & ROOM ALTERATIONS

(Completed 2020)

• SECURITY FENCING (Completed 2023)





PROJECT MEETING HISTORY

Grant K-8 Site Master Planning & Whole Site Modernization Phase I meetings in 2013:

- May 9, 2013: Task Force 1st Community Meeting
- May 13, 2013: Student Workshop Meeting
- May 14, 2013: Presentation to PTA
- May 23, 2013: Task Force 2nd Community Meeting
- June 6, 2013: Task Force 3rd Community Meeting
- June 13, 2013: Meeting with Teachers
- June 20, 2013: Task Force 4th Community Meeting

Whole Site Modernization Phase II meetings from 2023 to Today:

- June 13, 2023: Meeting w/ Principal for project start-up
- August 9, 2023: Meeting w/ Principal
- August 30, 2023: Meeting w/ Principal
- March 6, 2024: Presentation to Staff
- April 9, 2024: Presentation to Parents at PTA Meeting
- June 7, 2024: Programming Meeting w/ Staff



PORTABLES GRADES 6-8



(from 04/09 Presentation)



BLDG. 700 CLASSROOMS K-5

> BLDG. 600 CLASSROOMS K-5

AN.

BLDG. 500

PORTABLES GRADES 6-8

> BLDG. 600 FOOD SERVICE, CAFETERIA

















(from 04/09 Presentation)

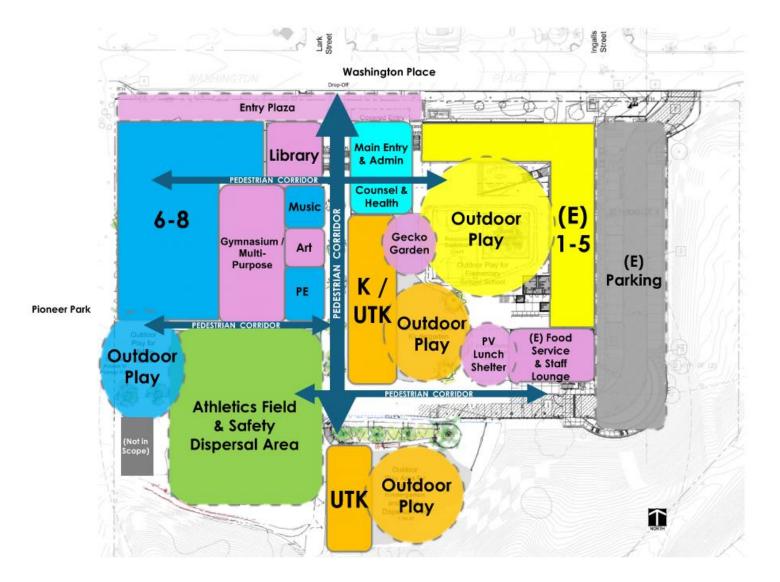






(from 04/09 Presentation)

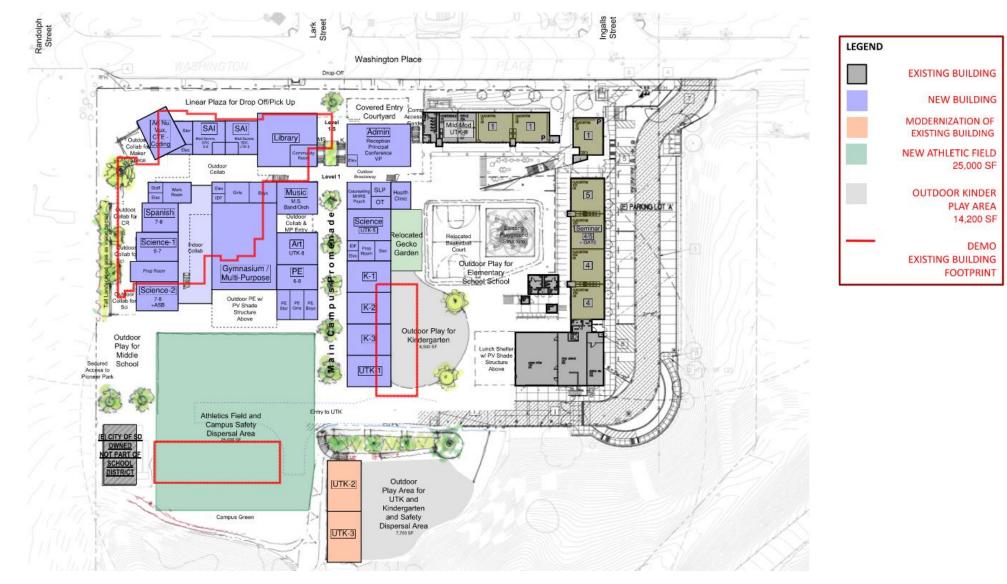





(from 04/09 Presentation)

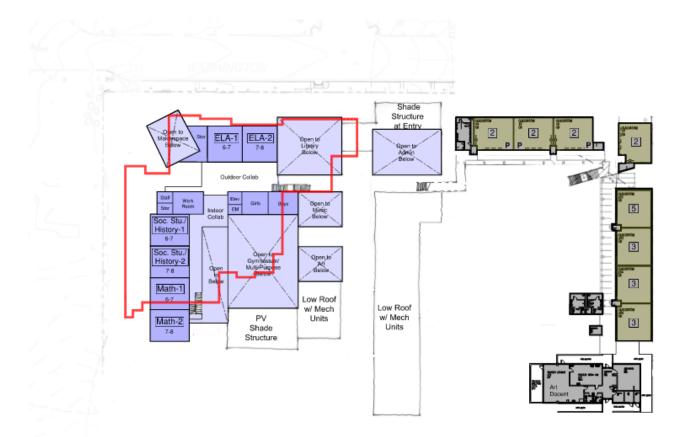











(from 04/09 Presentation)

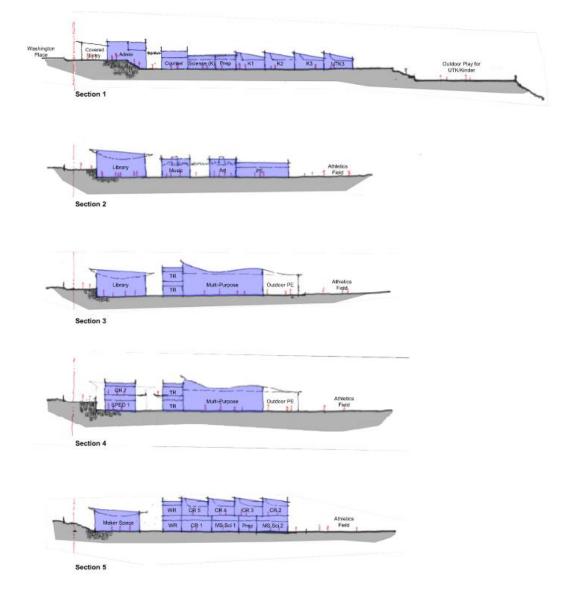


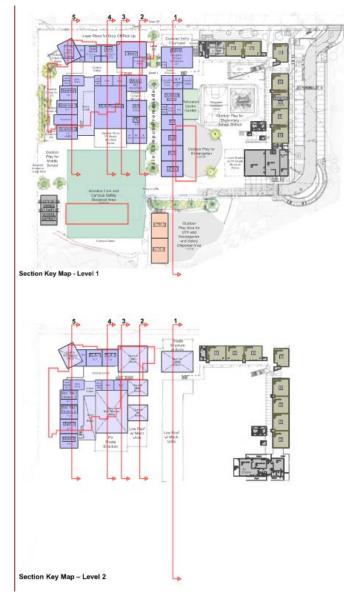





(from 04/09 Presentation)

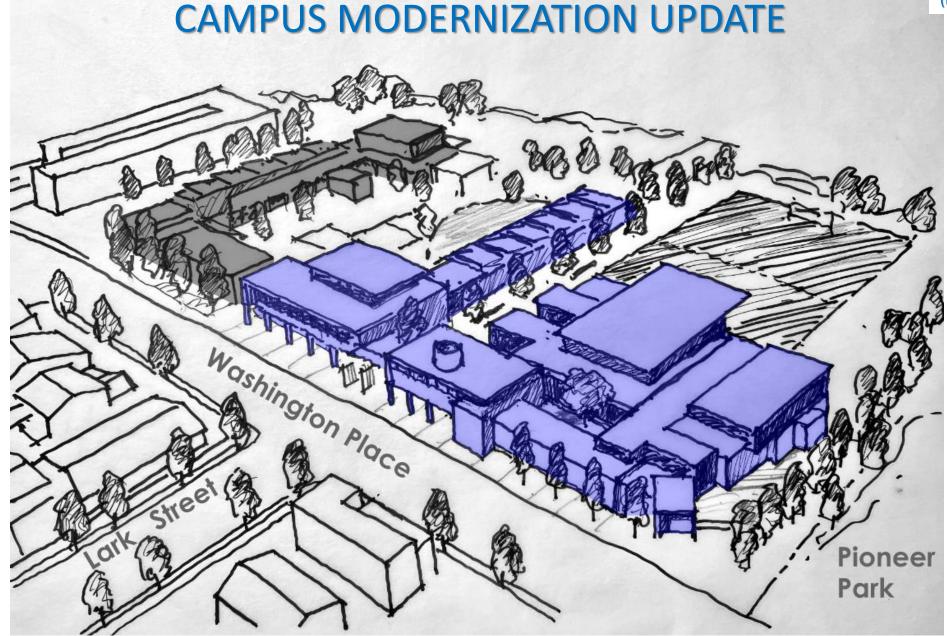





LATEST DRAFT OF SITE PLAN










MASSING STUDY

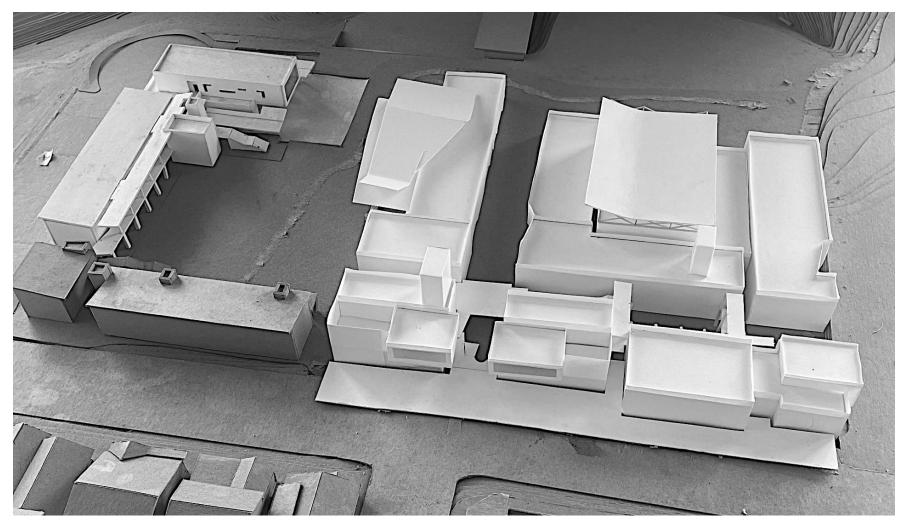





Fire Truck Access Lane

Limited Access for Contractors during later phases of construction

> Limited Access for Contractors during early phases of construction


Fire Truck Access Lane

Safe Dispersal Area






LATEST DRAFT OF PHASING

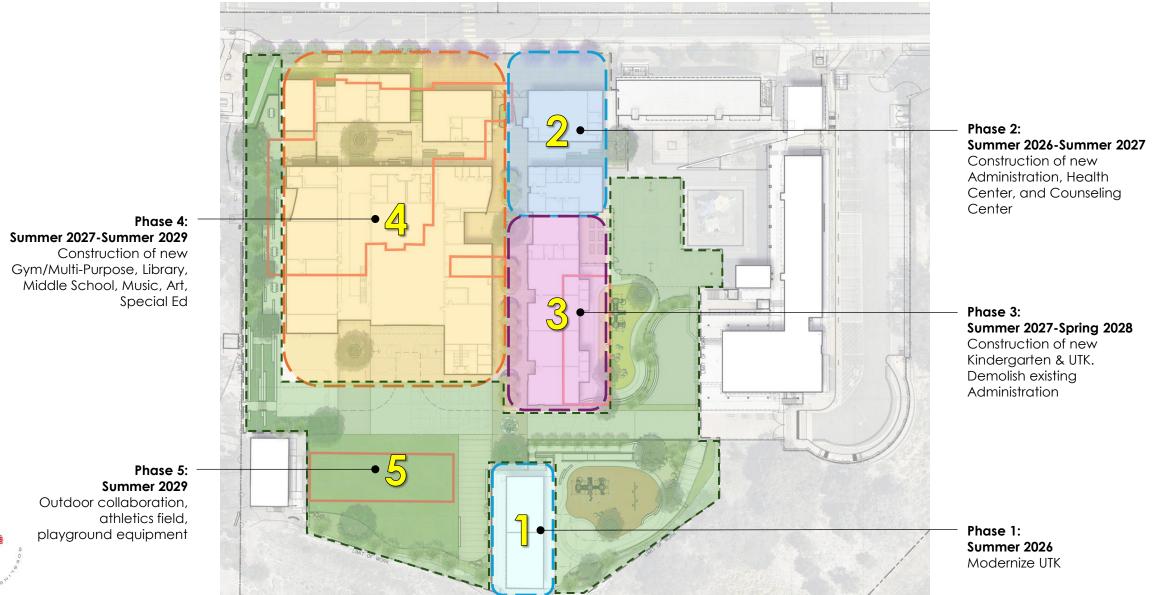





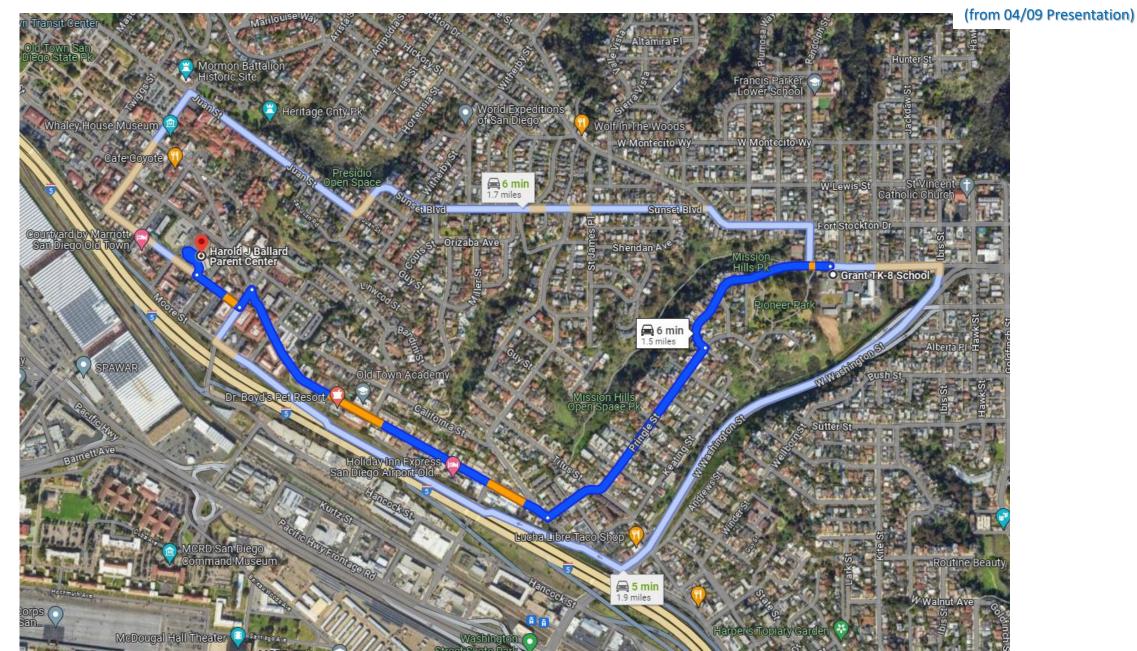





GRADES 6-8 INTERIM HOUSING







GRADES 6-8 INTERIM HOUSING









(from 04/09 Presentation)

PROJECT TIMELINE

PROJECT DESIGN/CONSTRUCTION PROCESS



	MAY	JULY	SP	RING	SPRING	i SUMMER	
	2024	2025	2	026	2029	2029	
WSM	DESIGN / CONSTRUCTION PLANS		DSA REVIEW / BID	CONSTRUCTION		MOVE BACK	
		Δ			Δ		



GRANT UTK-8 SITE MODERNIZATION

Questions/ Comments?



