Field

ID	Task Name	Duration	Start	Finish	Predecessors
1	Construction Fence	3 days	Tue 2/20/18	Thu 2/22/18	
2	Biological Fencing	3 days	Fri 2/23/18	Tue 2/27/18	1
3	Clearing and Grubbing	6 days	Wed 2/28/18	Wed 3/7/18	2
4	Grading	17 days	Thu 3/8/18	Fri 3/30/18	3
5	CIP Concrete Wall	10 days	Mon 4/2/18	Fri 4/13/18	4
6	Drain System	5 days	Mon 4/16/18	Fri 4/20/18	5
7	Irrigation System	20 days	Mon 4/23/18	Fri 5/18/18	6
8	Topsoil	5 days	Mon 5/21/18	Fri 5/25/18	7
9	Mow Curb	15 days	Mon 5/28/18	Fri 6/15/18	8
10	DG	10 days	Mon 6/18/18	Fri 6/29/18	9
11	AC Repair	5 days	Mon 7/2/18	Fri 7/6/18	
12	Planting	4 days	Tue 7/3/18	Fri 7/6/18	
13	Fencing	15 days	Mon 7/9/18	Fri 7/27/18	
14	Cleanup	10 days	Mon 7/30/18	Fri 8/10/18	
15	Demobilization	15 days	Mon 8/13/18	Fri 8/31/18	

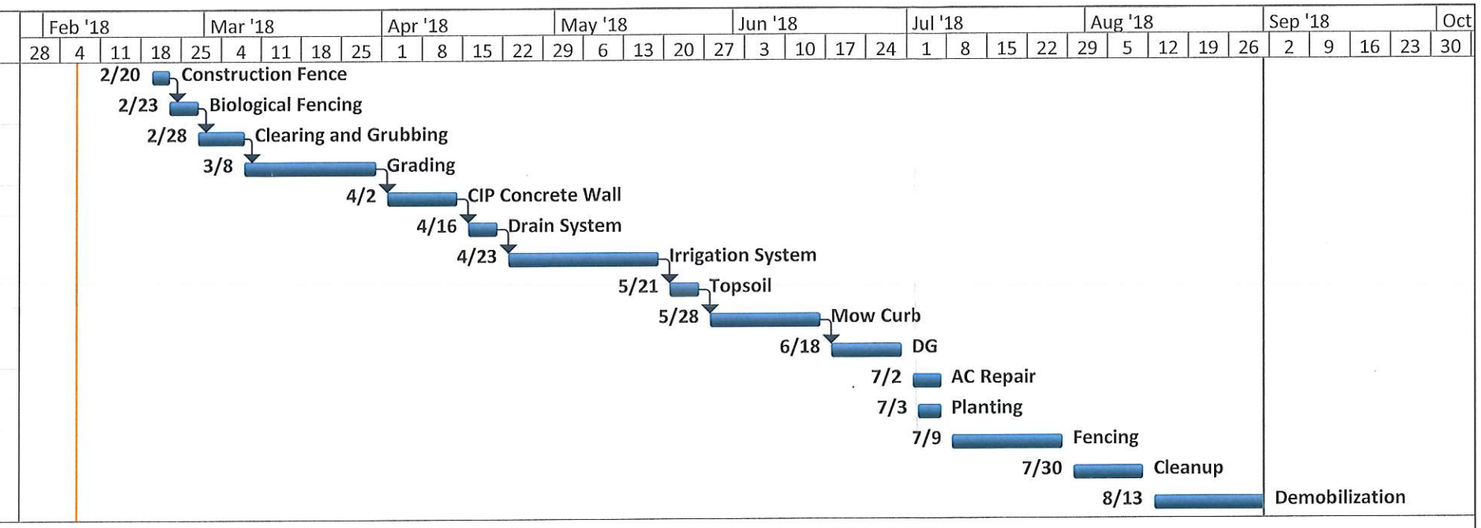

Project: Horton JUF 2
Date: Wed 2/7/18

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			
